# Jefferson School District
# Board of Education
# Facilities Update
# November 8, 2011

## Measure J Planning, Design and Construction

**Meeting Activities:**

Facility and Construction Planning Meetings: Monthly team meetings (District, PJHM & RGM) are scheduled for generally the 4th week of each month. Last meeting was on 9/22/11, next meeting is November 17, 2011.

Site Committee meetings: Met with the Jefferson School Planning Committee on 11/1/11.

**Project Status:**

1. Jefferson School Planning
   At the 11/1/11 meeting, we reviewed the schematic site plan and discussed the process of focused planning groups (ie. administration, standard classrooms, PE/Gym, Science, music, food service, etc). During these focus group meetings, educational specifications will be developed which will be the guiding factor in the design of the facilities. It was agreed that we will begin meeting with the focus groups in December.
   Next steps: • Schedule meetings with focus groups

2. Master Keying Project
   Bids Opened 11/2/11
   2 bids were received, however we may need to be rebid - due to contractor errors/irregularities on bid forms
   Construction over winter break

3. Hawkins Gymnasium Divider
   Bids Opened on 11/3/11
   1 responsive bid was received that was within the estimated budget
   Construction over Thanksgiving or winter break

4. Running Paths & Tracks @ Hawkins, Monticello & Traina
   DSA Backcheck will be completed on Wednesday 11/9/11.
   Bid and Construction schedule to be determined and coordinated
   Completion anticipated by fall/winter of 2012

5. Shade Structures @ Hawkins, Monticello & *Traina
   Projects were approved by DSA on 10/20/11

pjhm.architecture
OC// 24461 Ridge Route Drive #100 • Laguna Hills CA 92653 P// 949-496-6191
SD// 804 Pier View Way #103 • Oceanside CA 92054 P// 760-730-5527
PJHM.COM

Jefferson School District
Board of Education
Facilities Update
November 8, 2011

* DSA requires fire sprinklers for structure located at Traina stage
Bid and Construction schedule to be determined and coordinated
Completion anticipated by end of summer 2012

6. Hawkins Modernization
Construction documents in progress
DSA submittal next week (November 17)
Bid and Construction schedule to be determined and coordinated
Completion anticipated by fall/winter of 2012

7. Monticello Modernization
Construction documents in progress
DSA submittal next week (November 17)
Bid and construction schedule to be determined and coordinated
Completion anticipated by fall/winter of 2012

pjhm.architecture

OC// 24461 Ridge Route Drive #100 • Laguna Hills CA 92653 P// 949-496-6191
SD// 804 Pier View Way #103 • Oceanside CA 92054 P// 760-730-5527

PJHM.COM

# Jefferson School District Measure J

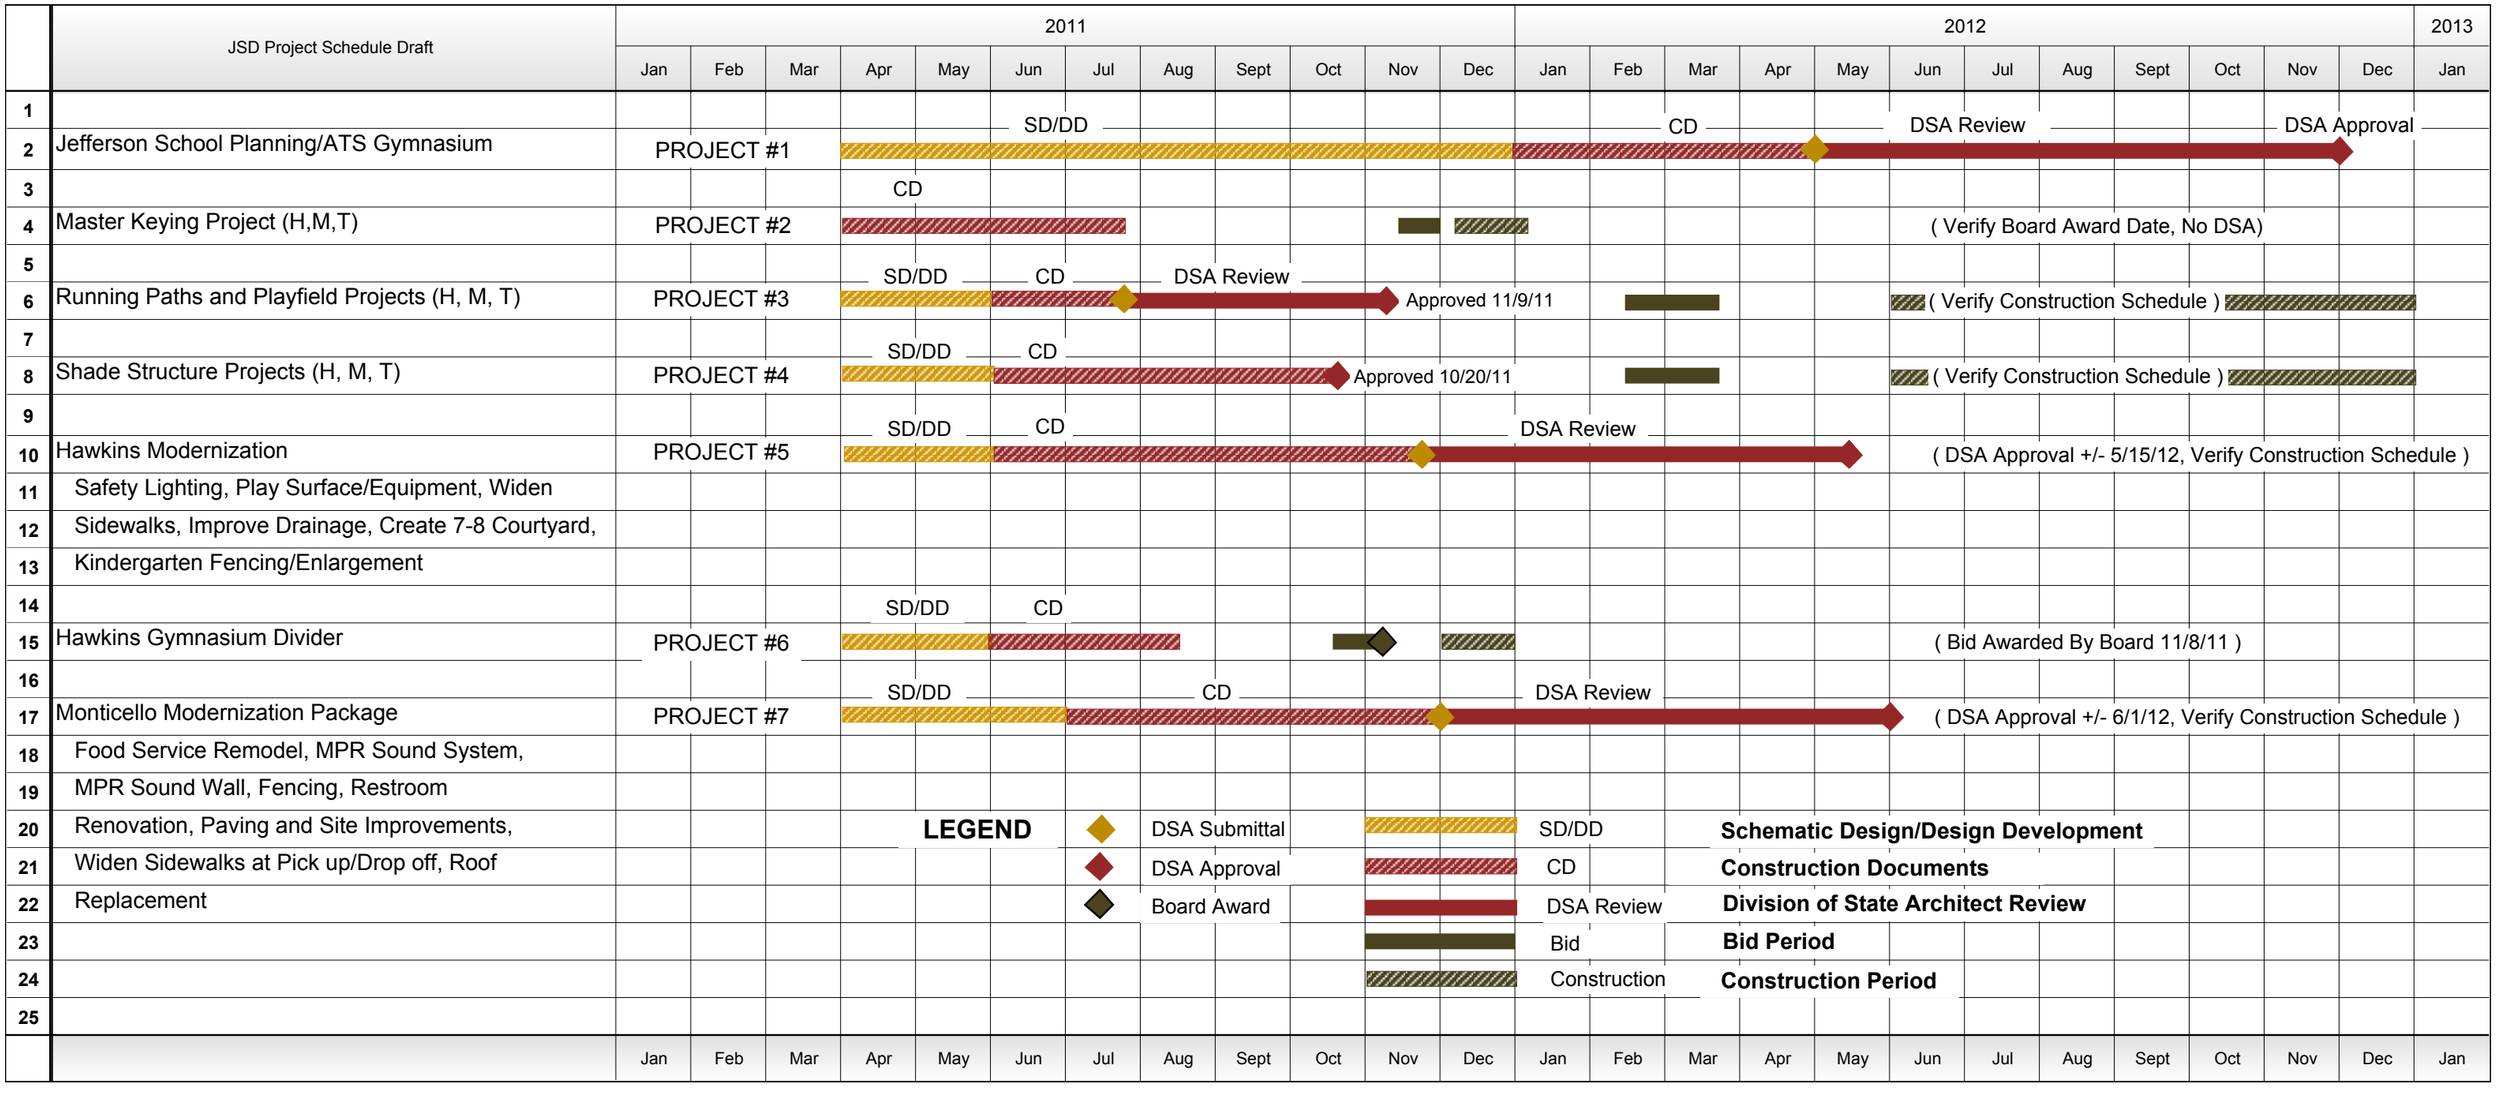


pjhm·architects

December 5, 2011

## MASTER PLAN CAPACITY:

700 STUDENTS

## INITIAL PHASE CAPACITY:

ACCOMMODATE CURRENT ENROLLMENT OF 460 STUDENTS IN 20 CLASSROOMS

## SCHEMATIC SITE PLAN (October 10th, 2011)

***RESULT OF PLANNING COMMITTEE INPUT FROM 9 / 21 / 11 MEETING***

- EXISTING STRUCTURE TO REMAIN
- NEW PROPOSED STRUCTURE
- RELOCATE EXISTING STRUCTURE TO NEW PROPOSED LOCATION

SCALE 10 20 60 100 150

pjhm·architects

# JEFFERSON SCHOOL PROJECT

JEFFERSON SCHOOL DISTRICT

PJHM.COM
